

Project: Gantt POB Caffaro

Date: Wed 17/04/19

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Path Predecessor Milestone Task

Path Predecessor Summary Task


Path Predecessor Normal Task

Deadline

Progress

Manual Progress

Page 1

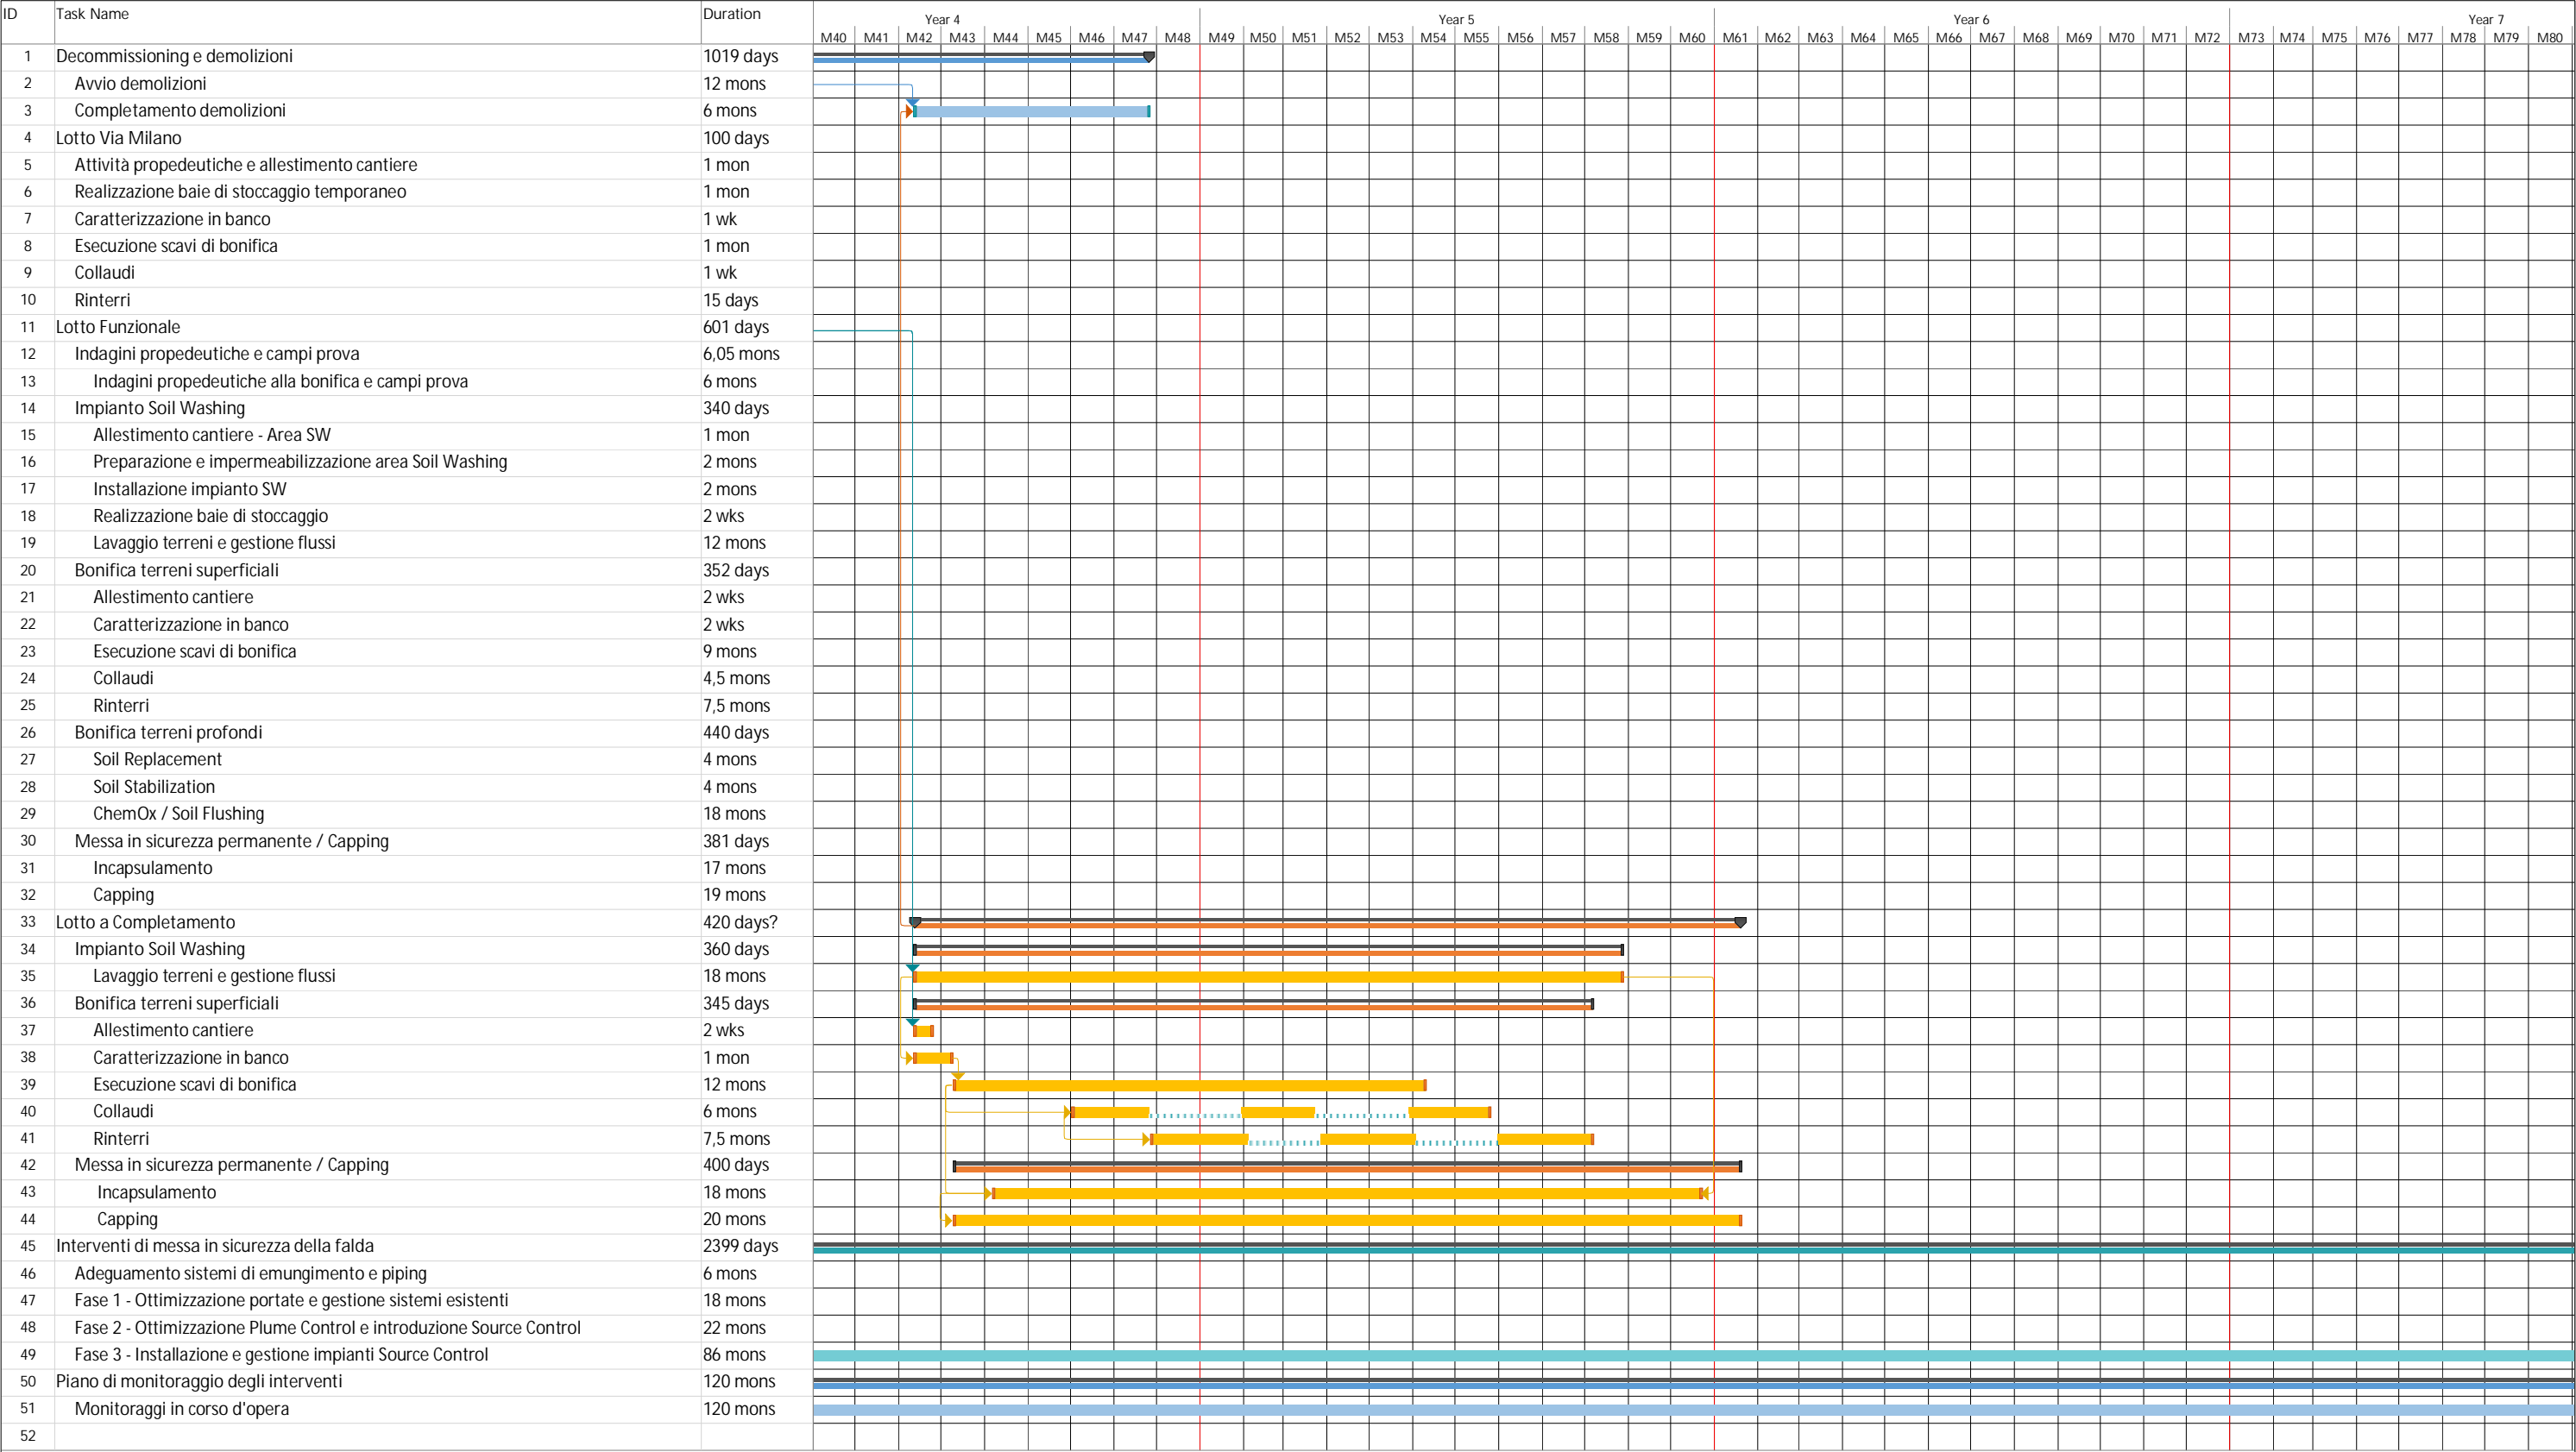

Project: Gantt POB Caffaro
Date: Wed 17/04/19

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Path Predecessor Milestone Task

Path Predecessor Summary Task

Path Predecessor Normal Task

Progress

Manual Progress

ID	Task Name	Duration	Year 8																Year 9												Year 10														
			M81	M82	M83	M84	M85	M86	M87	M88	M89	M90	M91	M92	M93	M94	M95	M96	M97	M98	M99	M100	M101	M102	M103	M104	M105	M106	M107	M108	M109	M110	M111	M112	M113	M114	M115	M116	M117	M118	M119	M120	M121		
1	Decommissioning e demolizioni	1019 days																																											
2	Avvio demolizioni	12 mons																																											
3	Completamento demolizioni	6 mons																																											
4	Lotto Via Milano	100 days																																											
5	Attività propedeutiche e allestimento cantiere	1 mon																																											
6	Realizzazione baie di stoccaggio temporaneo	1 mon																																											
7	Caratterizzazione in banco	1 wk																																											
8	Esecuzione scavi di bonifica	1 mon																																											
9	Collaudi	1 wk																																											
10	Rinterri	15 days																																											
11	Lotto Funzionale	601 days																																											
12	Indagini propedeutiche e campi prova	6,05 mons																																											
13	Indagini propedeutiche alla bonifica e campi prova	6 mons																																											
14	Impianto Soil Washing	340 days																																											
15	Allestimento cantiere - Area SW	1 mon																																											
16	Preparazione e impermeabilizzazione area Soil Washing	2 mons																																											
17	Installazione impianto SW	2 mons																																											
18	Realizzazione baie di stoccaggio	2 wks																																											
19	Lavaggio terreni e gestione flussi	12 mons																																											
20	Bonifica terreni superficiali	352 days																																											
21	Allestimento cantiere	2 wks																																											
22	Caratterizzazione in banco	2 wks																																											
23	Esecuzione scavi di bonifica	9 mons																																											
24	Collaudi	4,5 mons																																											
25	Rinterri	7,5 mons																																											
26	Bonifica terreni profondi	440 days																																											
27	Soil Replacement	4 mons																																											
28	Soil Stabilization	4 mons																																											
29	ChemOx / Soil Flushing	18 mons																																											
30	Messa in sicurezza permanente / Capping	381 days																																											
31	Incapsulamento	17 mons																																											
32	Capping	19 mons																																											
33	Lotto a Completamento	420 days?																																											
34	Impianto Soil Washing	360 days																																											
35	Lavaggio terreni e gestione flussi	18 mons																																											
36	Bonifica terreni superficiali	345 days																																											
37	Allestimento cantiere	2 wks																																											
38	Caratterizzazione in banco	1 mon																																											
39	Esecuzione scavi di bonifica	12 mons																																											
40	Collaudi	6 mons																																											
41	Rinterri	7,5 mons																																											
42	Messa in sicurezza permanente / Capping	400 days																																											
43	Incapsulamento	18 mons																																											
44	Capping	20 mons												</																															

Project: Gantt POB Caffaro
Date: Wed 17/04/19

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Path Predecessor Milestone Task

Path Predecessor Summary Task

Path Predecessor Normal Task

Progress

Manual Progress
